



project no: **18138**
project: **Church St James the Great**
site: **Lower Leigh Road, Westthoughton**

17 October 2019
18138/165/20:30/ VA

visit no: **004**
purpose of visit: **Site Inspection**
date/ time of visit: **17/10/19 2.30pm**
visit by: **Victoria Alderton**
contractor's rep: **Andy Sharp**

distribution: **Mr B. Latham**

1:00 Summary:

1:01 VA attended site on Thursday 17th October 2019, to review general progress.

2:00 Observations:

2:01 Reinstatement of west face of bell turret



a.

b.

Reinstatement of the west face of the bell turret is progressing well and stones are going back in place plumb and level. Underlying brickwork was treated for a final time with biocide prior to stones going back. (*images a. and b.*).




c.



d.

Raking out continues, however as mentioned in the previous report the hardness of the mortar is resulting in slow progress (*image c. & d.*).

Repointing has started at the lowest levels using the agreed mix, once 'green' the mortar will be brushed off to enhance the aggregate and give a coarser texture to the pointing. (*image e. & f.*).

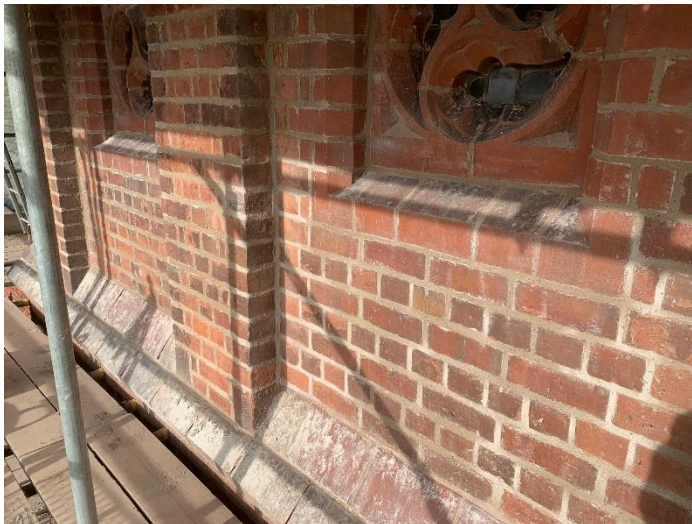

e.



f.
