



project no: **18138**  
project: **Church St James the Great**  
site: **Lower Leigh Road, Westthoughton**

13 Nov 2019  
18138/165/10:30/ VA

visit no: **005**  
purpose of visit: **Site Inspection**  
date/ time of visit: **13/11/19 9.30am**  
visit by: **Victoria Alderton**  
contractor's rep: **Andy Sharp**

distribution: **Mr B. Latham**


---

**1:00 Summary:**

1:01 VA attended site on Wednesday 13<sup>th</sup> November 2019, to review general progress.

**2:00 Observations:**

2:01 Ongoing repointing;

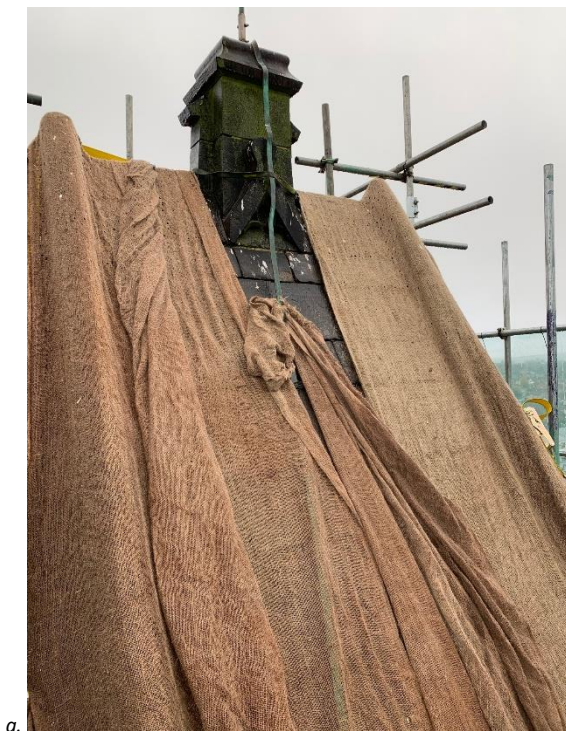

Work has progressed in earnest on the repointing; however, a spell of particularly wet weather has delayed progress, particularly at the top of the turret where it is to exposed to the elements to continue in the rain, and protection to joints has been necessary. (*image a.*)





c.



d.

Repointing at lower levels where the scaffold provides some protection to the elements has continued at pace. However, the wet weather means it is taking longer for the pointing to dry sufficiently for brushing off and cleaning down (*image b., c., d., e., & f.*). All replacement bricks have now been installed, delivery of the replacement terracotta units is still awaited.



e.



f.
