



AIR SAMPLING TEST CERTIFICATE

9608

Certificate Job Number: N-06219-001

Customer Name & Address	Contractor Name & Address	Site Address	Work Location
RS Asbestos, Ground Floor, Canal Wharf, Bacup Road, Todmorden, OL14 7PN	RS Asbestos, Ground floor, Canary Wharf, Bacup Road, Todmorden, OL14 7PN	St Peters Church Firs Lane Leigh WN7 4SB	Within base of main organ.
Start Date & Time:	25/02/2022 08:45	Site Lab Location:	Mobile Lab - Vehicle Reg: HL210BE

Site Conditions & Equipment Used

Microscope no.:	363	NPL test slide:	235	Graticule Diameter (µm):	100	Telescope no.:	389
Exposed filter diameter (mm)	22.5	Timer ref:	317	Flow meter ref:	315/316	Counter ref:	313/314
Barometer ref:	317	Thermometer ref:	317	Stage micrometre:	312	Band 5 visible:	YES
Site Pressure(mbar):	1023	Temperature (°C):	7	Filter Batch No.:	242		

SCOPE OF WORK

Reassurance air test conducted following encapsulation to panels within base of main organ

Air monitoring

Sample no.	Pump no.	Cowl no.	Test	Location	Start time	Finish time	Sample time (T)	Initial flow (l/m)	Final flow (l/m)	Average flow (F) (l/m)	Volume (V) (V=T*F)	Fibres	Fields	Limit of quantification	Calculated result (f/ml)	Recorded result (f/ml)
1	442	L10	Reassurance	Base of main organ	08:55	09:55	60	8.0	8.0	8.0	480	1.5	200	0.010	0.0008	< 0.01
2	N/A	L05	Field Blank	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	0	0	N/A	N/A	N/A

Acknowledgement

Pass or fail statement:	PASS Reassurance Air testing has proved to be satisfactory		
Analyst name:	Kevin Breithaupt	Signature:	
Finish Date & Time:	25/02/2022 10:20		
UKAS Accredited Method Statement and Disclaimers:	We hereby certify that site assessment for reoccupation has been carried out in accordance with the Health and Safety Executive's HSG248 and the E.S.S.S. Ltd SOP 2		

(#) UNCERTAINTY OF MEASUREMENT: The lower limit of quantification for the above method is stated in HSG248 as about 0.01 fibres/ml. When the sample volume is equal to or greater than 480 litres and 200 graticule fields are examined, a calculated result below the limit of detection may be expressed as <0.01 f/ml. For sample volumes below 480 litres and graticule field counts below 200, the lower limit of accurate measurement will be higher.

(*) ACTUAL FLOW RATE: Determined by averaging the calibrated Intermediate flow rates and/or where differences in ambient temperature and/or pressure between the calibration and sampling sites are greater than 5%.




9608

AIR SAMPLING LAYOUT DRAWING

Certificate Job Number: N-06219-001

Customer Name & Address	Contractor Name & Address	Site Address	Work Location
RS Asbestos, Ground Floor, Canal Wharf, Bacup Road, Todmorden, OL14 7PN	RS Asbestos, Ground floor, Canary Wharf, Bacup Road, Todmorden, OL14 7PN	St Peters Church Firs Lane Leigh WN7 4SB	Within base of main organ.
Start Date & Time:	25/02/2022 08:45	Site Lab Location:	Mobile Lab - Vehicle Reg: HL210BE

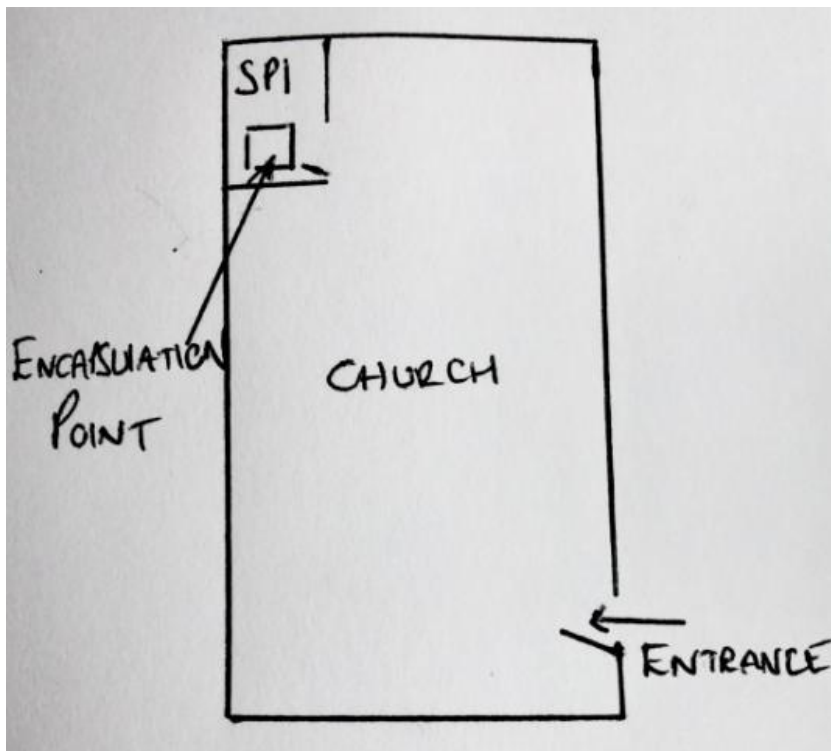

KEY							
DIAGRAMS MUST BE INCLUSIVE OF APPROXIMATE ENCLOSURE DIMENSIONS							
Enclosure:	EN	Waste Skip:	WS	Waste Route:	WR	Negative pressure unit:	NPU
Viewing Panel:	VP	Work area:	WA	Airlock:	AL	Transit route:	TR
LARC Van:	LV	Hygiene facility:	HF	Baglock:	BL	Sample point:	SP

We the undersigned agree that the diagram is an accurate indication of the site layout for the project.

Contractor name:	J.Molloy	Contractor signature:	
Date:	25/02/2022		
Analyst name:	Kevin Breithaupt	Analyst signature:	
Date:	25/02/2022		



9608

AIR SAMPLING PHOTOGRAPHS

Certificate Job Number: N-06219-001

Customer Name & Address	Contractor Name & Address	Site Address	Work Location
RS Asbestos, Ground Floor, Canal Wharf, Bacup Road, Todmorden, OL14 7PN	RS Asbestos, Ground floor, Canary Wharf, Bacup Road, Todmorden, OL14 7PN	St Peters Church Firs Lane Leigh WN7 4SB	Within base of main organ.
Start Date & Time:	25/02/2022 08:45	Site Lab Location:	Mobile Lab - Vehicle Reg: HL210BE



SP1 in operation
with
encapsulated
panels in
background



9608

AIR SAMPLING SITE DIARY

Certificate Job Number: N-06219-001

Customer Name & Address	Contractor Name & Address	Site Address	Work Location
RS Asbestos, Ground Floor, Canal Wharf, Bacup Road, Todmorden, OL14 7PN	RS Asbestos, Ground floor, Canary Wharf, Bacup Road, Todmorden, OL14 7PN	St Peters Church Firs Lane Leigh WN7 4SB	Within base of main organ.
Start Date & Time:	25/02/2022 08:45	Site Lab Location:	Mobile Lab - Vehicle Reg: HL210BE

REPORT DETAILS

Include any variations from standard procedures, relevant environmental conditions that significantly influenced results, any incidents of elevated fibre levels, required actions resulting from any incidents etc

No additional notes were deemed necessary to be captured whilst on this site visit.

(Opinions & interpretations expressed herein are outside the scope of our UKAS accreditation)
